



Proposed Residential Development
Land off Cork Lane
Glen Parva
Leicestershire

Design stage site waste management plan

Cedar Barn, White Lodge,
Walgrave,
Northampton,
NN6 9PY

T: 01344 781811
F: 01344 781999
E: mail@jppuk.net
W: jppuk.net

Proposed Residential Development
Land off Cork Lane
Glen Parva
Leicestershire

Design stage site waste management plan

JPP Consulting Ltd., Cedar Barn, White Lodge, Walgrave, Northampton, NN6 9PY

T: 01344 781811

F: 01344 781999

E: mail@jppuk.net

W: jppuk.net

Report Reference R-SWMP-R6711PP-01

Date January 2014

Report Originators

Prepared by



Marin Andrews MEng (Hons)

Project Engineer

martin.andrews@jppuk.net

Reviewed by



Philip A Brown BEng (Hons) CEng MICE MCIHT MCIWEM CWEM

Director

phil.brown@jppuk.net

Contents

Report Section	Principal coverage	Report status	
		Page no	Revision
1	Introduction	3	
2	Project Information	5	
3	Responsibilities	7	
4	Waste minimisation	8	
5	Forecast	9	
6	Waste management options	10	
7	Implementation	12	

List of appendices	
A	Proposed Masterplan RG+P drawing no. 7779/005C

1.0 Introduction

- 1.1 The Client has legal duty to prepare, update and implement a Site Waste Management Plan (SWMP) is set out in the Site Waste Management Plans Regulations 2008 (SI 2008 no.314) which came into effect on 6 April 2008. In accordance with these Regulations any client intending to carry out a construction project on one site with an estimated cost greater than £300,000 must, before work begins, prepare a SWMP with a more detailed plan being required for projects with an estimated cost greater than £500,000.
- 1.2 JPP Consulting has been appointed by Manor Oak Homes to prepare the design stage SWMP. The Principle Contractor, upon appointment, shall then be responsible for maintaining and updating the SWMP in accordance with the statutory regulations.
- 1.3 SWMPs apply to all aspects of construction work including preparatory work such as demolition and excavation. They are required for civil engineering and engineering projects as well as projects involving the maintenance, alteration and decoration of existing structures. The installation, maintenance or removal of all related services such as electrical, gas, water, sewage and telecommunications are also subject to this requirement. Routine maintenance operations such as gully cleaning or grass cutting, as opposed to maintenance of a structure, do not fall within this scope. A full description of the range of activities to which this measure applies is provided in the SWMP Regulations.
- 1.4 The SWMP outlined below has been developed as design stage SWMP. It identifies the following:
- Who will be responsible for resource management
 - What types of waste are likely to be generated and predicted volumes.
 - What likely targets can be achieved for the reduction of waste with respect to the reduction, reuse, recovery, recycling and disposal.
- 1.5 The proposed residential development comprises 166 residential dwellings and associated public open space. The proposed development is shown on the plan enclosed in Appendix A.

1.6 Site Location Plan

1.6.1 Figure 1.6.1 presented below shows the location of the site.

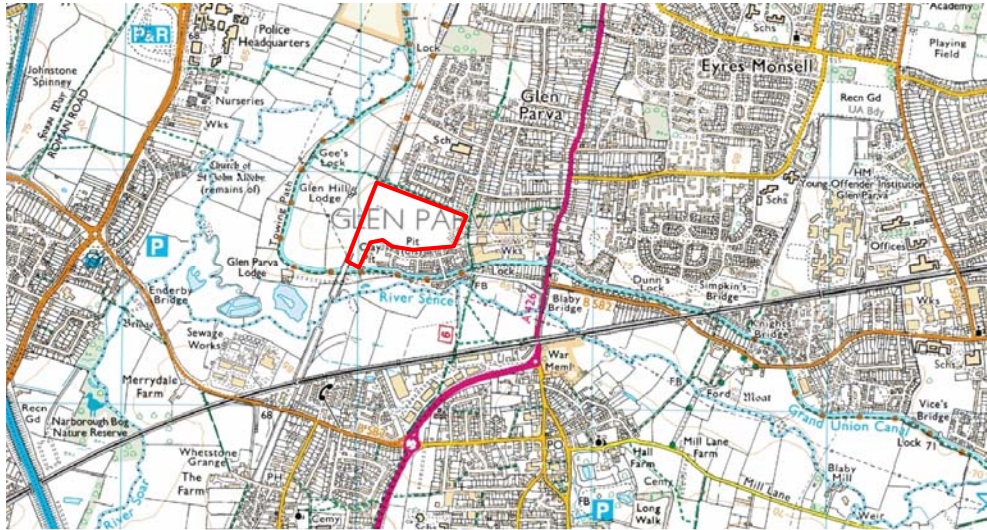


Figure 1.6.1, Site location plan. Approximate site boundary outlined in red.

2.0 Project Information

2.1 Project Name:

Land off Cork Lane, Glen Parva, Leicestershire

2.2 Project Location:

Land off Cork Lane
Glen Parva
Leicestershire
EAST MIDLANDS

2.3 Client (Developer):

Manor Oak Homes
William Main
White Lodge Farm
Walgrave
Northampton
NN6 9PY
T: 01604 781 457

2.4 Principal Contractor:

To be appointed

2.5 Architect:

RG+P Limited
130 New Walk
Leicester
LE1 7JA
T: 01344 500 040

2.7 Engineer:

JPP Consulting
Consulting Civil and Structural Engineers
Cedar Barn
White Lodge
Walgrave
Northampton
NN6 9PY
T: 01604 781 811

2.8 Project Details

2.8.1	Classification:	Residential
2.8.2	Project use class:	Houses
2.8.3	Client Type:	Developer
2.8.4	Project Type:	New build
2.8.5	Project start date:	2016
2.8.6	Construction Type	Load bearing masonry
2.8.7	Code for Sustainable Homes:	Current version – Nov 2010

2.9 Estimated Project Costs (ex. VAT)

2.9.1 £13,650,000

2.10 Floor Areas (m²):

2.10.1 19,100

2.11 Site Area (Ha):

2.11.1 10.550ha

2.12 Site Description:

2.12.1 Greenfield previously used as landfill

2.13 Other requirements

None.

2.14 Where the SWMP is to be kept:

On site and readily available to all interested parties.

3.0 Responsibilities

3.1 SWMP Initial draft:

The Engineer
Martin Andrews
JPP Consulting

3.2 Final Version:

The Principal Contractor

3.3 SWMP Implementation:

The Developer
William Main
Manor Oak Homes

3.4 Waste Champion:

The Principal Contractor

3.5 Person in charge of the project:

The Developer
Manor Oak Homes

3.6 Declaration:

We agree that the 'Client' and the 'Principal contractor' shall take all reasonable steps to ensure waste duty of care is complied with, material are handled efficiently and waste is managed appropriately, all in accordance with the statutory regulations in force at that time.

Name and signature: William Main

On behalf of: Manor Oak Homes

Date:

Name and signature: Martin Andrews
MEng (Hons)

On behalf of: JPP Consulting

Date: 2nd January 2014



4.0 Waste minimisation

4.1 Table 4.1 below outlines decisions made before drafting the plan on the nature of the project, design, construction methods and materials to plan waste minimisation.

Type	Waste Minimisation decision taken	By whom	Intended results
Reduction in excavated material off site	To carry out a cut and fill analysis of the development	Engineer	Designing proposed levels to reduce excavated material likely to be removed from site.
Carry out a detailed ground investigation	To accurately identify the ground conditions of the site	Geo-environmental engineer	To accurately identify contamination and to develop an appropriate remediation strategy.
	Carry out CBR testing	Geo-environmental engineer	To minimise pavement thickness.
	To accurately identify the ground conditions of the site	Geo-environmental engineer	To accurately design foundations.
Carry out a tree survey	To reduce foundation excavations	Arboriculturalist	To accurately design foundations.
	Off site manufacture of joinery items	Contractor	Reduce timber wastage and off cuts.
	Reuse wall insulation off cuts in roof insulation	Contractor	Re-use insulation to reduce off site disposal.

Table 4.1

5.0 Forecast

5.1 The table below estimates the types and amounts of waste expected to be generated on this project. As these are generally unknown at this stage, table 5.1 below is based on benchmarks using a floor area of 6,900m² for a residential development.

Waste Forecast	
Product	Volume (m3)
Bricks	325.9
Tiles and Ceramics	32.3
Concrete	285.2
Inert	425.2
Insulation	120.7
Metals	168.7
Packaging	68.4
Gypsum	266.1
Binders	19.6
Plastics	137.6
Timber	537.1
Floor coverings (soft)	23.2
Electrical and electronic equipment	9.3
Furniture	4.5
Canteen/office/adhoc	113.5
Liquids	4.1
Oils	0.2
Asphalt and tar	25.5
Hazardous	37.1
Other	98.5
Mixed	669

Table 5.1

6.0 Waste management options

6.1 Waste reduction targets shall be set and agreed prior to the commencement of works on site. Disposal of waste shall be measured against the key target performance indicators, current at the time of developing the construction phase SWMP. Waste reduction targets shall be expressed as shown in table 6.1 below:

Waste reduction targets					
Waste Type	Reduce (%)	Reuse (%)	Recover (%)	Recycle (%)	Dispose (%)
Bricks					
Tiles and Ceramics					
Concrete					
Inert					
Insulation					
Metals					
Packaging					
Gypsum					
Binders					
Plastics					
Timber					
Floor coverings (soft)					
Electrical and electronic equipment					
Furniture					
Canteen/office/adhoc					
Liquids					
Oils					
Asphalt and tar					
Hazardous					
Other					
Mixed					
Total					
Table 6.1					

6.2 As a guide the waste reduction targets outlined above in table 6.1 shall be as follows:

Waste reused	= 22%
Waste recycled	= 14%
Waste recovered	= 35%
Waste disposed	= 29%

The percentage reduction targets will depend on many factors including the project type and construction methods to be employed, purchasing rules etc. The above target percentages are the average waste diversion from landfill figures, and % management routes for all projects completed on SMARTWaste.

7.0 Implementation

The Principal Contractor shall be responsible for implementing the SWMP to include the following. The lists are not exhaustive and more information may be required to satisfy other requirements, for example, WAS 2 of the Code for Sustainable Homes.

7.2 Duty of Care

It is a mandatory requirement to include Duty of Care in the SWMP. Both the Client and Principal Contractor shall take reasonable steps to ensure waste and materials are handled correctly. The following shall be recorded

- Waste Management Contractor name and address.
- Waste Carrier licence number, date of issue and expiry date.
- Waste management licence number, date of issue and expiry date.
- Waste transfer notes storage location.

7.3 Waste Records

It is mandatory to record and identify the following:

- Who the person removing the waste from the site is.
- the type of waste.
- where the waste has been taken to and if the site has a waste management licence or exemption.
- Waste carrier licence number.
- Evidence e.g. waste transfer note.

7.4 Waste Log

It is mandatory to record at least every six months the type and quantities of waste produced and the quantities of waste and what has happened to the waste. The definitions used in Section 6 shall be used to define the waste, recorded as volumes or by weight. The type of waste shall be recorded as follows:

- Re-use on site
- Re-use off site
- Recycling on site
- Recycling off site
- Recovery on site
- Recovery off site
- Sent to landfill
- Other disposal

7.5 Training

Everyone on site shall receive the appropriate training that shall include a training log detailing the training given and how it will be delivered and to who. An up to date copy shall be kept on site and made available on request.


7.6 Review

The SWMP shall be reviewed and checked regularly with record being kept to demonstrate this and record the outcomes and any recommendations from these outcomes. The SWMP shall be reviewed at not less than every six months.

Appendix A
Site Plan
rg+p drawing no. 7779 005C

Site Area = 10.55 ha
 Development Area = 6.09 ha
 POS & Area of Natural Open Space = 4.46 ha
 Total Number of Dwellings = 165 units
 Site Density = 27 p/ha

- A Layout modified to reduce development area following comments from engineers & client SA 11.10.13
- B Focal routes introduced to west side of development SA 17.10.13
- C Property against the eastern boundary removed for pedestrian link to Cork Lane; private drives on south and east broken with green space. Additional planting and boundary treatment around car park areas. Play area location modified; site ownership red line modified. SA 26.02.14

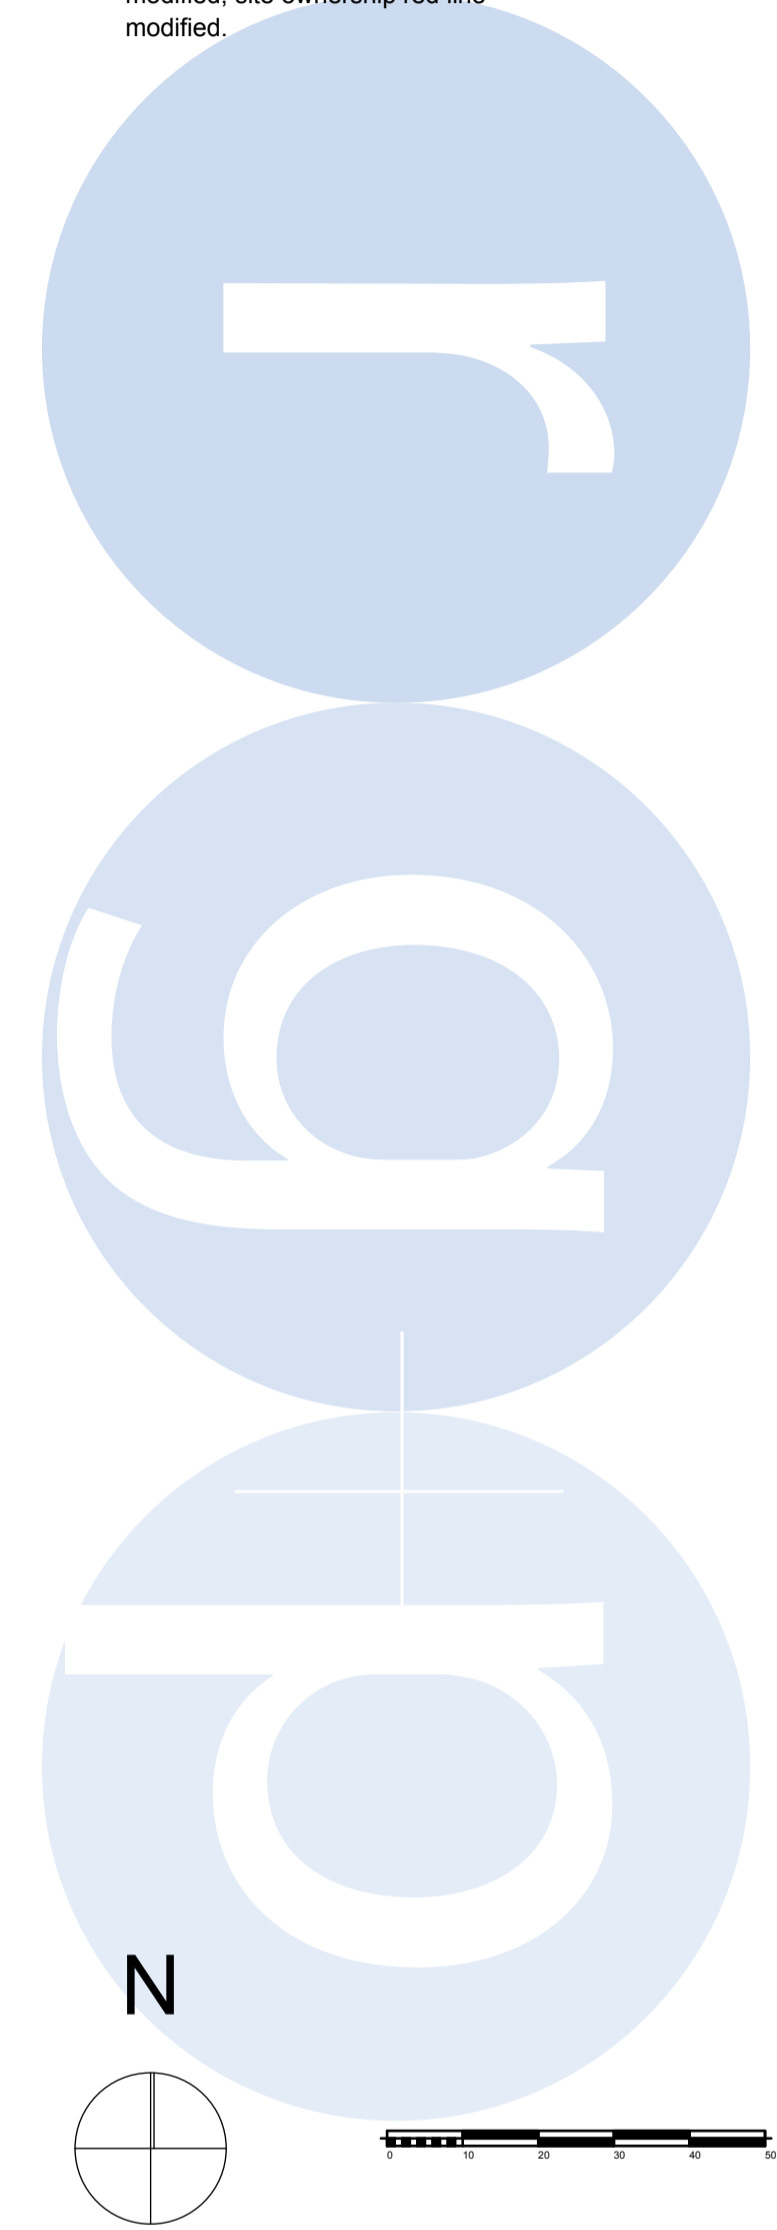

Architects · Project Managers · Quantity Surveyors
 130 New Walk
 Leicester, LE1 7JA
 Tel: 0116 204 5800, Fax: 0116 204 5801
 email: design@rg-p.co.uk, www.rg-p.co.uk

Project: Residential Development
 Cork Lane, Glen Pava

Client: Manor Oak Homes

Sheet title: Proposed Masterplan

Ref: 7779 / 005 C

Scale: 1:1000 @ A1

Date: 27/09/13

Drawn: SA Checked: RAW
